

Final Project Completion Report

Project Name and Number: 1453 East 9400 South Well and 8518 South 960 East Well Pump Replacements, #4051

Description: Replacement of pumping equipment and well rehabilitation at the 1453 East 9400 South Well and 8518 South 960 East Well. The mechanical and chemical development resulted in a 12.9 percent increase in specific capacity at the 1453 East 9400 South Well and a 6.3 percent increase in specific capacity at the 8518 South 960 East Well.

District Project Manager: Kevin Rubow

Engineer:	CRS Engineers	Design Status: 100%
Original Engineering Contract Amount:		\$45,400
Final Engineering Contract Amount:		\$49,900

Summary of Engineering Amendments:		
	<u>Description</u>	
1	Additional engineering and construction management services.	\$4,500
	Total Amendments Amount:	\$4,500


Contractor:	Widdison Turbine Service, LLC	Construction Status: 100%
Original construction contract amount:		\$847,697
Total Change Order amount:		-\$46,588
Current construction contract amount:		\$801,109
Total change orders as a percentage of original contract:		-5.5%
Completion Schedule:		
	Notice to Proceed:	10/10/2017
	Final Completion:	2/4/2019

Summary of Change Orders:		
	Description	Amount
1	Credit for pumping equipment draw-down test.	-\$51,528
2	Replacement of roof shingles at the 1453 East 9400 South Well.	\$4,940
	Total Change Order Amount:	-\$46,588

Final Project Completion Report



Removing existing column pipe

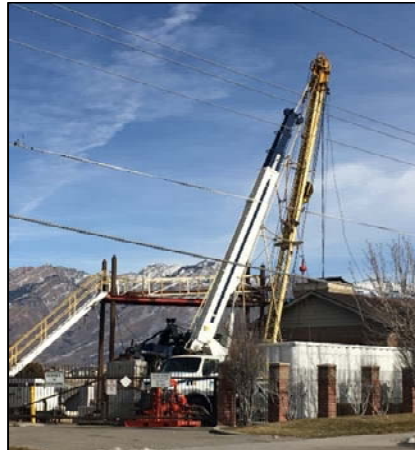

Performing mechanical development



Installing new pump



Pump discharge head



Crane off-loading column pipe



Testing new pump
