

Final Project Completion Report

Project Name and Number: Landscape Improvement - 108 East 11400 South, #4079

Description: Design and installation of landscape improvements for the 108 East 11400 South pump station site. Areas of existing turf were converted to water-wise landscaping.

District Project Manager: Kevin Rubow

Engineer:	JWCD Staff	Design Status: 100%
Original Engineering Contract Amount:	Not applicable	
Current Engineering Contract Amount:	Not applicable	

Contractor:	WKB Landscape, Inc.	Construction Status: 100%
Original construction contract amount:		\$26,800
Total Change Order amount:		\$8,372
Final construction contract amount:		\$35,172
Total change orders as a percentage of original contract:		31.2%
Completion Schedule:		
Award of Purchase Order:		5/3/2019
Final Completion:		1/2/2020

Summary of Change Orders:		
	Description	Amount
1	Asphalt Replacement at the 108 East 11400 South pump station.	\$8,024
2	Replacement of the existing gate keepers.	\$349
	Total Change Order Amount:	\$8,372




Final Project Completion Report



Graded site and staging of new plant material



Moonglow junipers

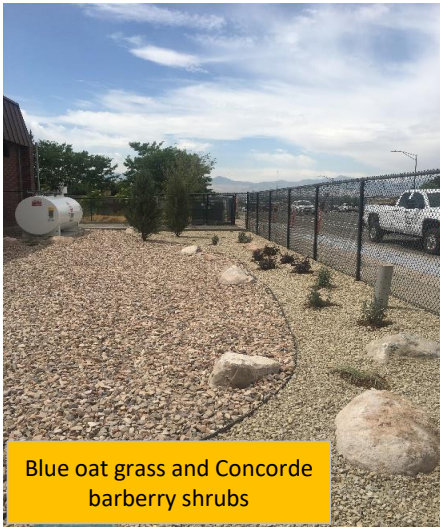

Blue oat grass and Concorde barberry shrubs



Ivory halo dogwood and landscape rock mulch



Removal of failing asphalt
